

D58 Sidewalk Plan

March 16, 2021



Background

- Residents submitted a petition for a sidewalk on the south side of Norfolk from Saratoga to Carpenter
- Village Council considered request on Sept. 15, 2020
- VC directed staff to prepare a plan for the construction of sidewalks near D58 schools
- The FY21 budget includes \$220k for this project



Sidewalk System Review

- Staff reviewed the existing sidewalk system in proximity of D58 schools
- For 30 years the Village had a policy of constructing a sidewalk on one side of every street
- As a result, all schools are served by sidewalks on at least one side of the surrounding streets
- These existing sidewalks were generally constructed on the side of the street with the fewest neighborhood impacts
- The proposed segments will require multiple neighborhood trade-offs



Sidewalk Construction Plan

- Staff evaluated many potential sidewalk segments and developed a proposed four-year plan
- Plan includes five segments at four schools
 - Consider as stand-alone projects
 - Each segment should be further evaluated for specific neighborhood trade-offs
 - Construct over next four years (2021 – 2024)
- D58 staff support this plan



Sidewalks to Consider as Stand Alone Projects

YEAR	SCHOOL	STREET	EST. COST	TRADE-OFF CONSIDERATIONS
2021	KINGSLEY	NORFOLK (Saratoga to Main)	\$120K - \$180K	TREE IMPACTS DRAINAGE SYSTEM PRIVATE PROPERTY IMPACTS
2022	FAIRMOUNT/O'NEILL	BLODGETT (59 th to 61 st)	\$90K - \$140K	TREE IMPACTS PRIVATE PROPERTY IMPACTS
2023	PIERCE DOWNER/ HERRICK	OAKWOOD (Grant to Ogden) GRANT (Oakwood to Saratoga)	\$200K - \$300K	TREE IMPACTS OVERHEAD UTILITIES STEEP SLOPES/WALLS PRIVATE PROPERTY IMPACTS
2024	HIGHLAND	FOREST (39 th to 40 th)	\$90K - \$130K	TREE IMPACTS PRIVATE PROPERTY IMPACTS
		TOTAL	\$500K - \$750K	

Decision Making Process

- Neighborhood trade-offs will be required in each location
- Each segment will undergo preliminary design
 - Specific trade-offs determined
 - Detailed cost estimate
 - Neighborhood input at public meeting
- Staff will present preliminary design to VC
- If VC wishes to proceed, design will be finalized and bids will be received for VC consideration





Kingsley Elementary School




2/18/2021





Fairmount Elementary School & O'Neill

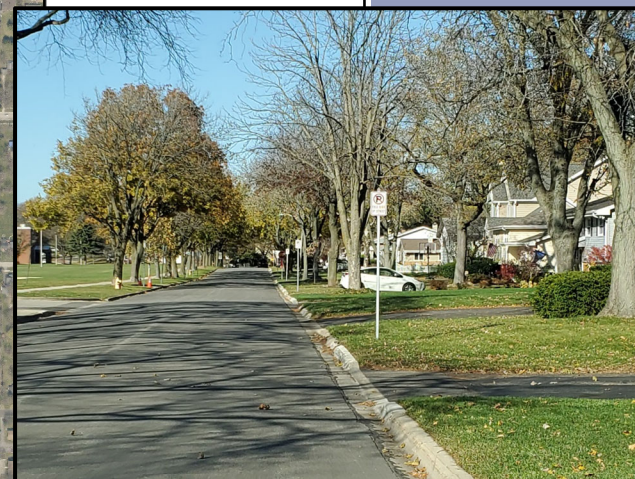

2/18/2021





Herrick Middle School




2/18/2021






Highland Elementary School

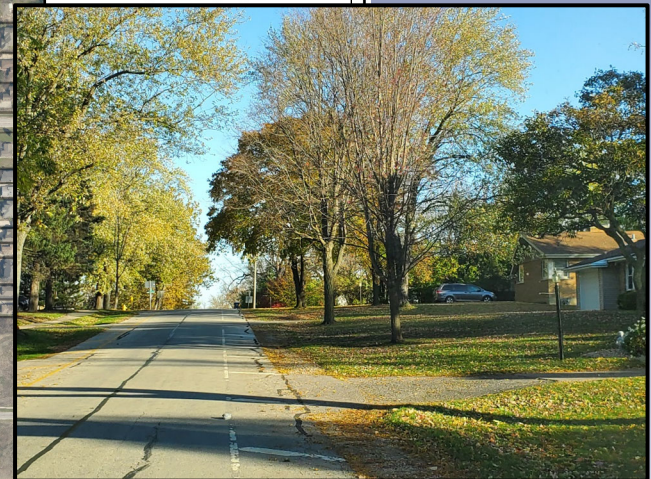

2/24/2021



Sidewalks to Consider w/Future Projects

- Staff also identified 20 sidewalk segments that should be considered in the future
- Staff will identify opportunities for including these with other projects
 - Water Main Replacement
 - Drainage
 - Roadway Reconstruction
- Each potential segment will be budgeted into the CIP as they are identified
- Staff will present trade-offs and cost to VC for consideration with overall project



Schedule for Norfolk Sidewalk

Neighborhood Meeting	April, 2021	Discuss Concept Design and Get Feedback
Preliminary Design of Sidewalk	May – June	Determine Trade-offs and Cost
VC Consideration	June	1st Go/No-Go Decision
Final Design and Bidding	July	
VC Consider Bids	August	2nd Go/No-Go Decision
Construction	September - October	

